Date: 3/27/2013 **Author:** S.ELLIOTT **Project:** HWY 19A / BAY AVE.

Comments:
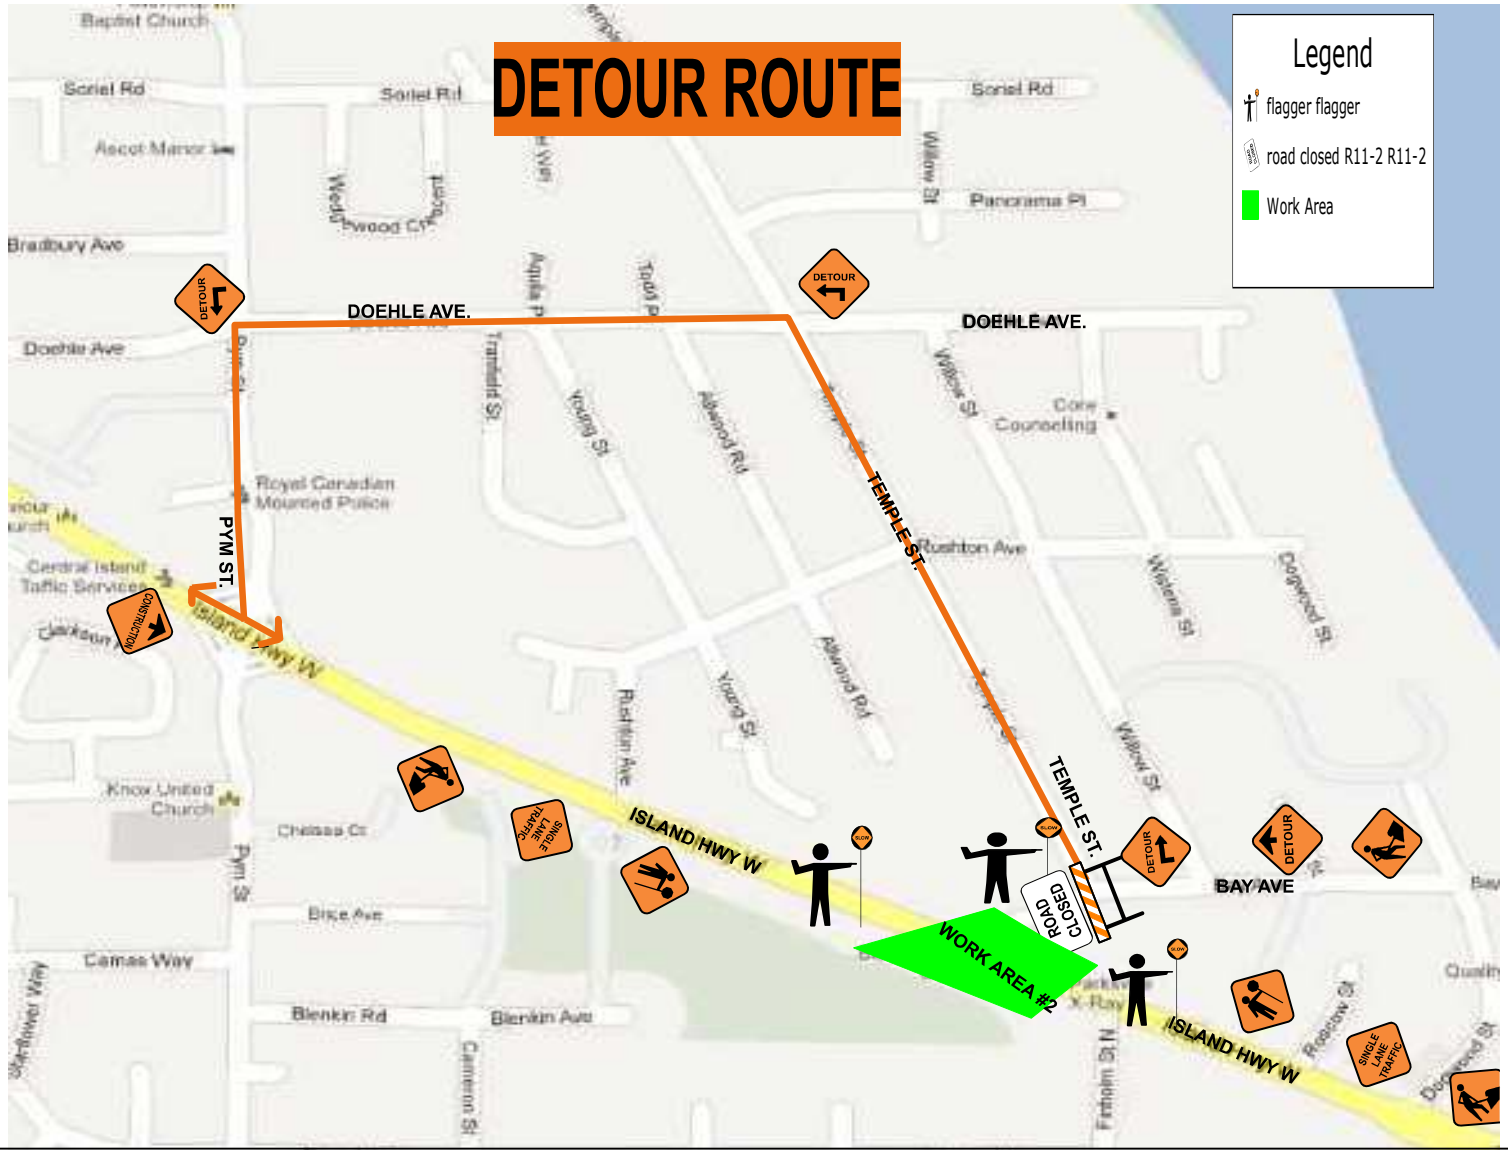
TCM - FIGURE 4.3.1 - Lane closure with TCP - Two Lane Two-Way Roadway.
TCM - FIGURE 4.5.3 Detour for One Lane Closed Two Lane Two-way Intersection
For work at Bay Ave. traffic will be detoured away from the work area
to reduce risks during peak construction TCP will maintain two-way traffic on HWY 19A whenever possible and maintain
single lane alternating during non peak traffic hours.
